
Enter building with PVC and pull box into mechanical room re-doing coax entry. Will need splice ticket. Install PTP on block wall in mechanical room. Install jumper 450ft along open ceiling trusses through multiple suites to rack in data room. Needs lift and has ramp. Some suites wont require lift.

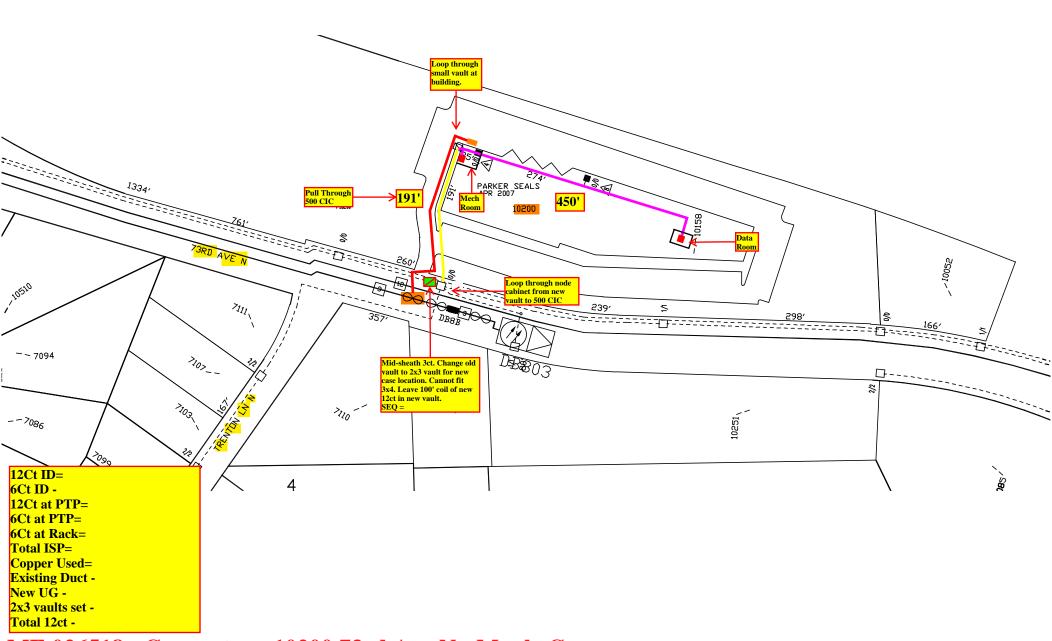

ME 026518 - Conventus - 10200 73rd Ave N - Maple Grove
